Weekly Report 2 – Inception

Sprint 1 12–18 October 2026
Group 2 – Medication Safety Assistant

Report date: 18 October 2026. **Project board:** `https://github.com/users/hyt2434/projects/3/views/1`
Planning baseline: Software Development Plan v1.0 and Vision Document v1.0, both dated 18 October 2026.

1 Weekly summary

The team reports raw medicine-data collection, preliminary processing, feasibility checks, refinement of the concept and requirements, and a UI prototype. The repository confirms planning-document commits on 16 October and frontend/prototype commits on 16–18 October. The submitted Software Development Plan and Vision Document are both version 1.0 dated 18 October; this report follows those updated baselines rather than treating the earlier commits as proof of final acceptance. The plan's Sprint 1 output is the PA1 package: Project Plan, Vision, 3–6 representative UI screens, two weekly reports and tracking evidence. The raw-data and feasibility outputs were described by the team but are not evidenced by a linked result in this report; attach their files, sample counts and measurements before claiming them as verified deliverables. At capture time, PA1 issues #11–#14 remained open in GitHub Project (#11 In Review, the rest In Progress).

2 Individual contributions

Cao Hoàng Long

Done tasks. Team-reported: collect raw DAV data, perform preliminary cleaning and feasibility checks, and refine the requirements and data approach. Add source/version, sample count, cleaning log and test result as evidence; the current issue/commit record does not independently confirm completion.

To-do tasks. 19–25 Oct, Sprint 2: review requirements, medication-data provenance and the Module 1–2 interface; prepare #44 – a shared input/output contract and expected–actual tests. Begin limited #45 – NLP intent and #46 – DAV normalization/ingredient mapping feasibility slices with measured outputs. #47 – Module 3 result-state design is optional; #48 – E2E smoke test is conditional. The full medication-safety PoC remains a Sprint 3 target.

Issues for team discussion. Discuss incomplete DAV records, brand-to-ingredient ambiguity, DDInter coverage, licensing/reuse rights and the Module 2/3 boundary: identification in Module 2; interaction and duplicate-ingredient assessment in Module 3.

Hoàng Yến Trang – Team Lead

Done tasks. Project Plan and Vision v1.0 are dated 18 October; the UI prototype and React frontend have 16–18 Oct commits. GitHub keeps #11 In Review and #12 In Progress, so the PA1 package still needs an acceptance review.

To-do tasks. 19–25 Oct, Sprint 2: review the main workflows, user-confirmation screens, module interface and tests; begin #41 – a limited OCR feasibility implementation/report for clear printed or digital prescriptions, with editable confirmation. Coordinate #48 – a smoke test only if prerequisite slices run. #43 – manual input is assigned to hyt2434 although its issue body plans Thành; reconcile that assignment.

Issues for team discussion. Discuss OCR image quality, privacy-safe test images and the shared confirmation schema. Handwritten prescription support is outside the initial release.

Lỗ Chí Thành

Done tasks. The team reports feasibility work on multimodal input. No personal implementation commit is visible in the exported Git log for this week; confirm the actual result and attach evidence.

To-do tasks. 19–25 Oct, Sprint 2: review voice/manual input requirements and module fields; begin #42 – voice-to-text feasibility and confirmation tests. #43 – manual entry with verified suggestions is planned for Thành in the issue body but currently assigned to hyt2434; confirm/reassign. Join #48 – the E2E smoke test only if the required slices are runnable. Reminder design may be reviewed now; full Module 5 implementation belongs to Sprint 5.

Issues for team discussion. Discuss Vietnamese medicine-name recognition, microphone permission, editable transcripts, verified suggestion data and manual fallback.

3 Current PA1 task register

Task	GitHub assignee(s)	Created	Due field	Last update	Name / current Project status
#11	hyt2434, DRAGON-1312	16 Oct	Not set	16 Oct 06:13 UTC	Plan and Vision; In Review
#12	hyt2434	16 Oct	Not set	16 Oct 03:39 UTC	3–6 UI screens; In Progress
#13	hyt2434, DRAGON-1312	16 Oct	Not set	16 Oct 03:39 UTC	Reports and PA1 package; In Progress
#14	hyt2434	16 Oct	Not set	16 Oct 03:39 UTC	Tools/tracking; In Progress

The issues' descriptions give a planned PA1 target of 18 October, but a distinct GitHub due-date field is not visible in the public Project/issue view. GitHub handles do not identify every team member with certainty; planned owners come from issue descriptions and the Project Plan. Screenshots below show name, description and assignee; exact creation/update timestamps are transcribed from the public GitHub API.

4 Next-week to-do: PA2, 19–25 October

The following PA2 issues were created in GitHub on 18 October. They are future to-do items, *not* completed Week 2 work. Their issue bodies specify a 19 October start and 25 October target, except #44's proposed 23 October target. These are target dates in issue descriptions, not a verified GitHub Project Due Date field. According to the updated Project Plan, 19–25 October is Sprint 2's *design-review* week: review requirements/workflows/architecture, agree on confirmation, interfaces, data formats, safety rules and test plans. Issue descriptions also ask for early implementation/feasibility work; treat any such work as a limited Sprint 2 slice, not as completion of the Sprint 3 modules. Build 0.1, integrating four input modes and safety checks, is targeted for 15 November.

Issue	Task / expected output	Current GitHub assignee	Planned owner	Created	Last update (UTC)
#41	OCR code, feasibility report and measured tests	hyt2434	Trang	18 Oct	09:46
#42	Voice-to-text code, report and confirmation tests	thanh12388h	Thành	18 Oct	09:46
#43	Manual input with validated suggestions	hyt2434	Thành	18 Oct	09:48
#44	Shared input/output contract and expected–actual tests	DRAGON-1312	Long	18 Oct	09:48
#45	Chatbot/NLP intent flow and constrained explanation	DRAGON-1312	Long	18 Oct	09:48
#46	DAV normalization, ingredient mapping and DDInter lookup feasibility	DRAGON-1312	Long	18 Oct	09:48
#47	Module 3 safety interface/result-state design (stretch)	DRAGON-1312	Long	18 Oct	09:48
#48	E2E smoke test across OCR, voice, manual and Module 2 (stretch)	hyt2434, thanh12388h, DRAGON-1312	Whole team	18 Oct	09:48

Issue details and acceptance criteria: #41 – OCR; #42 – voice; #43 – manual entry; #44 – shared contract; #45 – NLP; #46 – Module 2 data work; #47 – Module 3 design; #48 – E2E test. All eight issues were Open at verification time. #43's assignee differs from its planned owner and should be corrected or explicitly agreed by the team. Module 3 and

E2E are stretch tasks. In the Vision baseline, Module 2 identifies medicines/ingredients; Module 3 performs DDInter 2.0 drug–drug interaction and duplicate-ingredient checks. An unmatched or unassessed case must never be presented as safe. The initial release excludes handwriting OCR, ADR reporting, drug–food interaction checks and production healthcare integration.

Evidence follow-up: The Project screenshot below is an earlier 18 October capture of PA0/PA1 items and does not show the newly added PA2 rows. Before submission, attach a fresh Project screenshot and one issue-detail screenshot for each PA2 to-do task. The report table records the public issue metadata verified on 18 October; a distinct Due Date field remains unverified.

5 Git and Project evidence

Commit export: `evidence/commit-log-week-02.txt`. The export supports documentation and UI work only; no raw-data/feasibility implementation result should be inferred from a generic commit title. No PR linked to #11–#14 is visible in the Project screenshot.

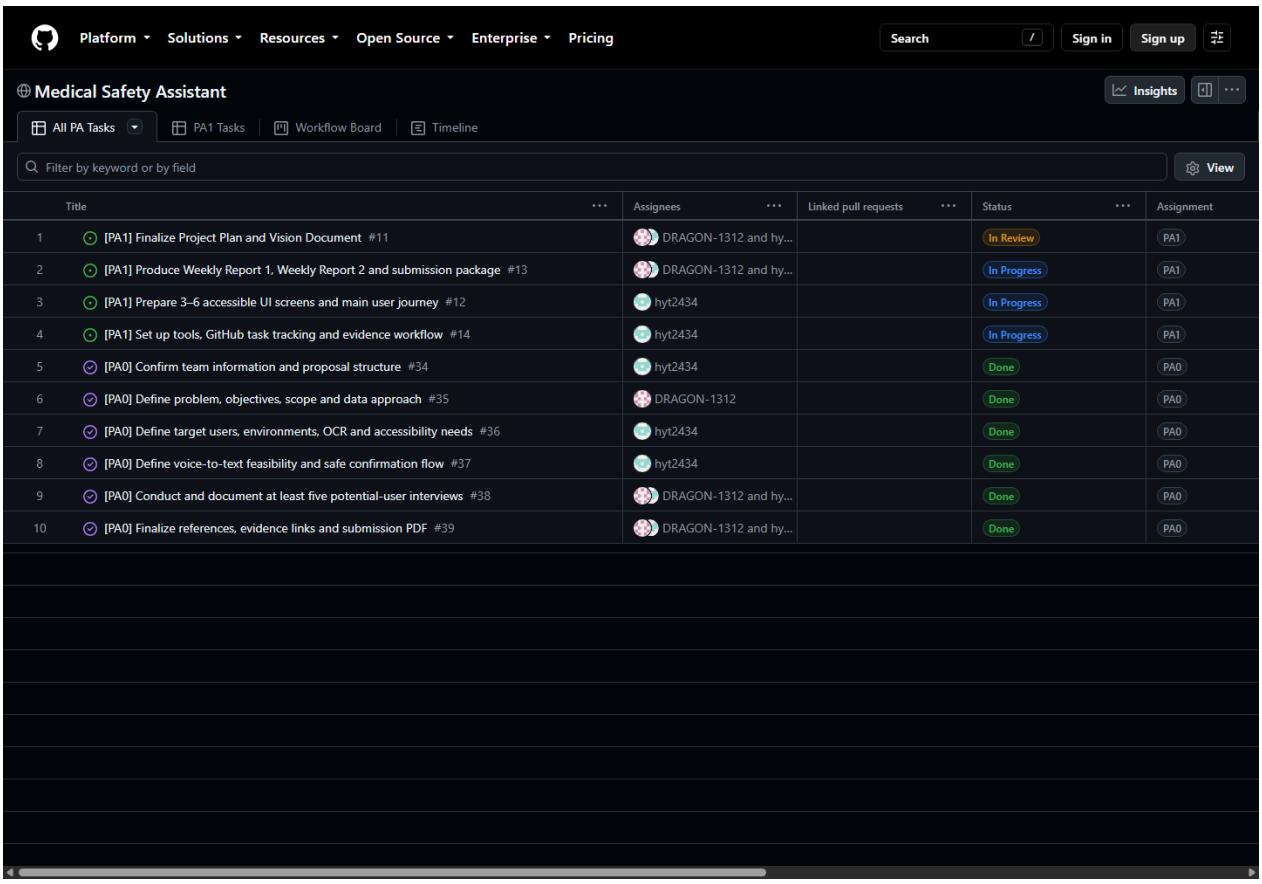


Figure 1: Public GitHub Project board, captured 18 October 2026. PA1 task statuses and assignees are visible.

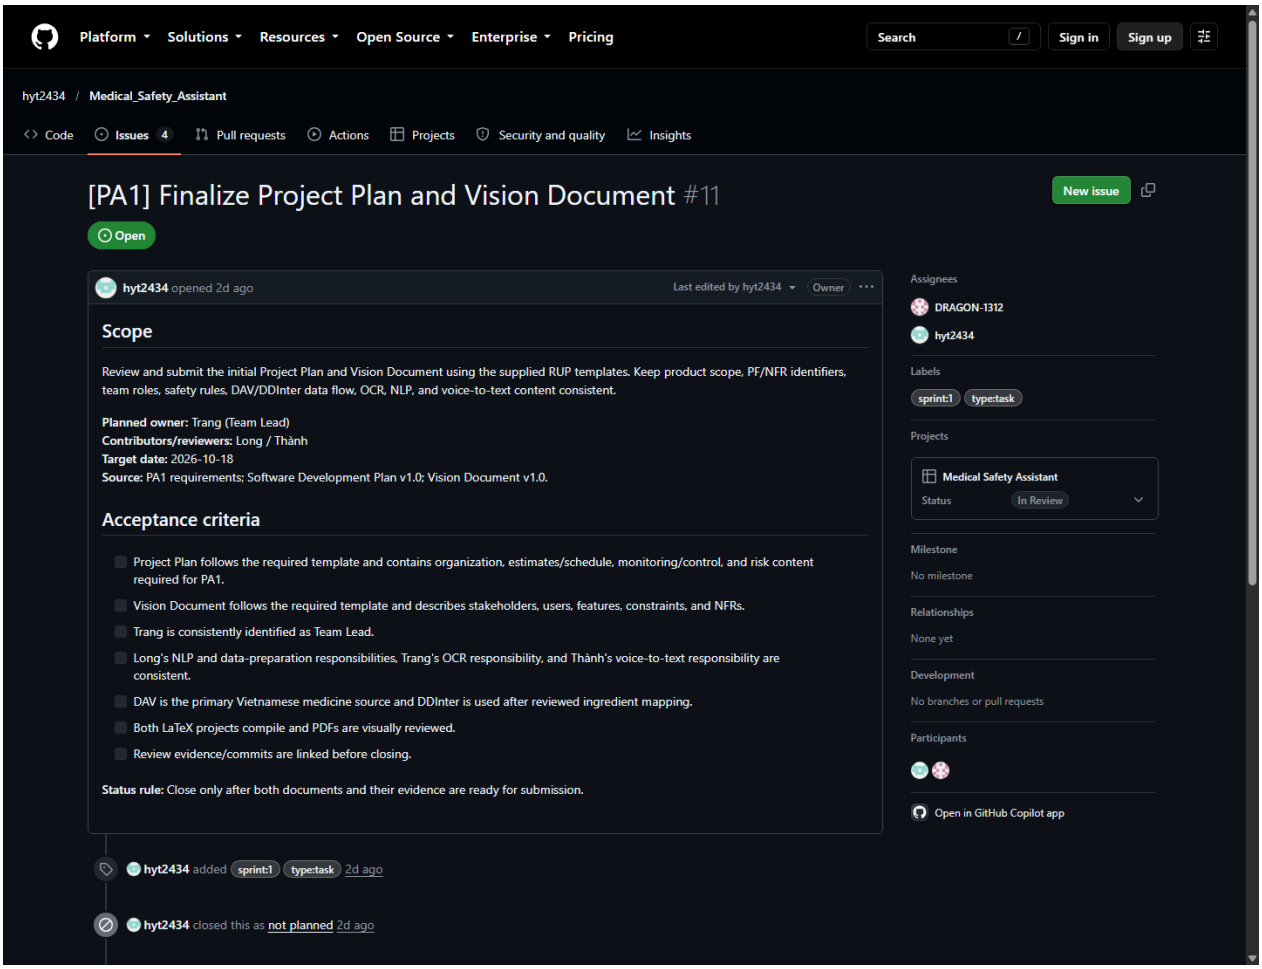


Figure 2: Issue #11: Project Plan and Vision scope, assignees, target in body and review criteria.

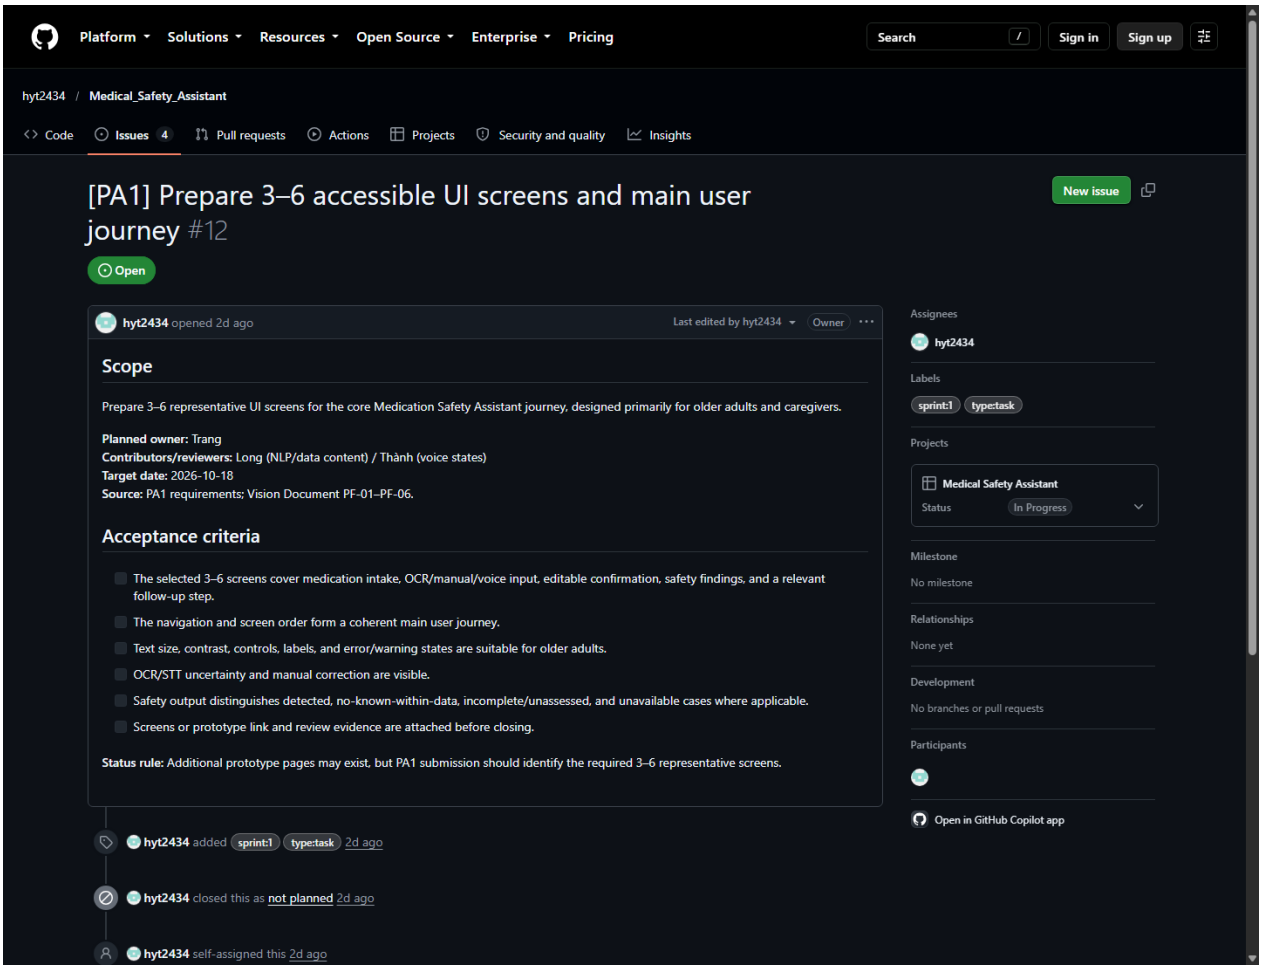


Figure 3: Issue #12: UI prototype task, scope, assignee and acceptance criteria.

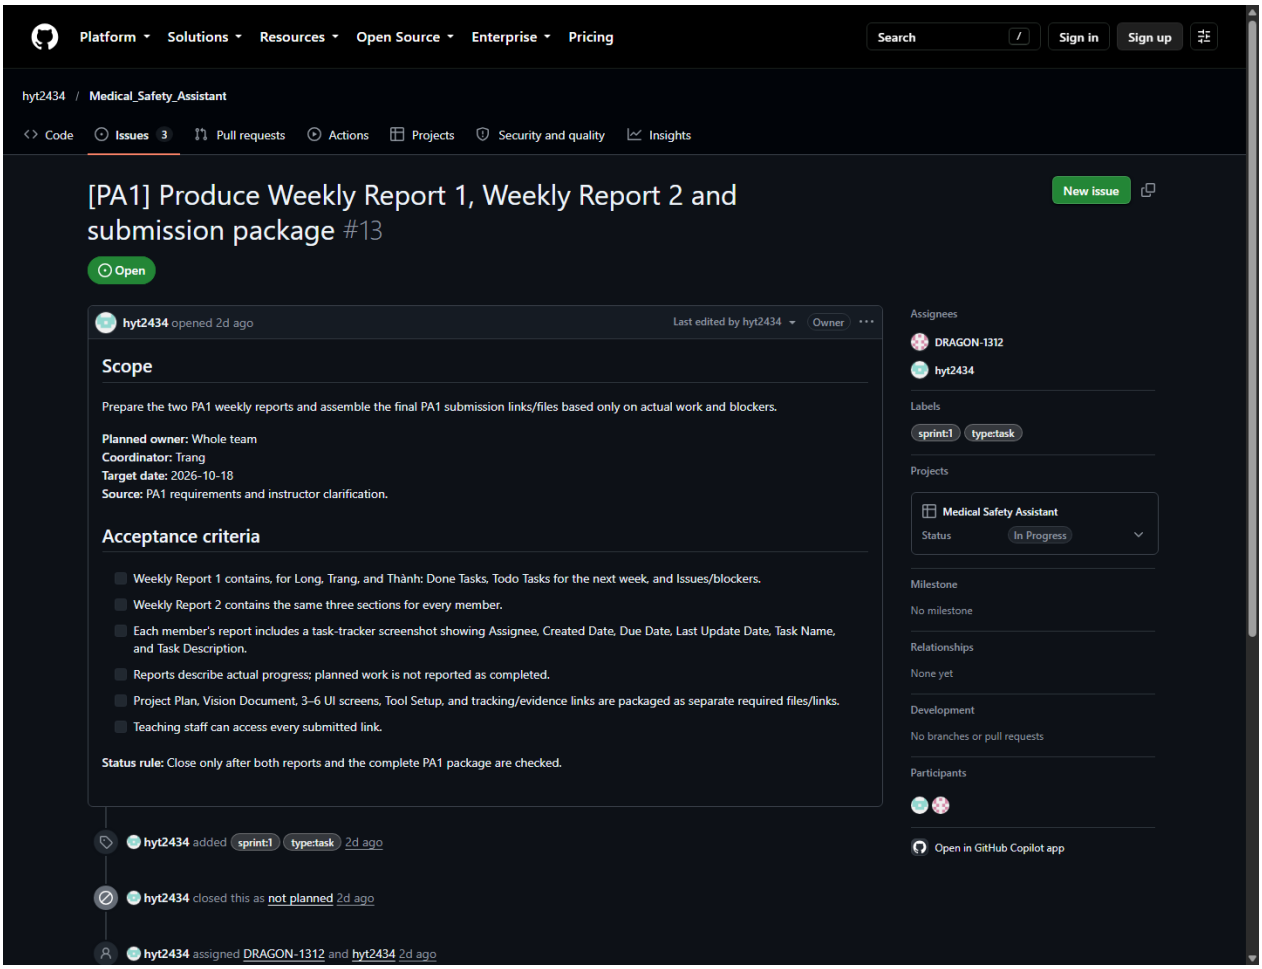


Figure 4: Issue #13: weekly reports and submission package task.

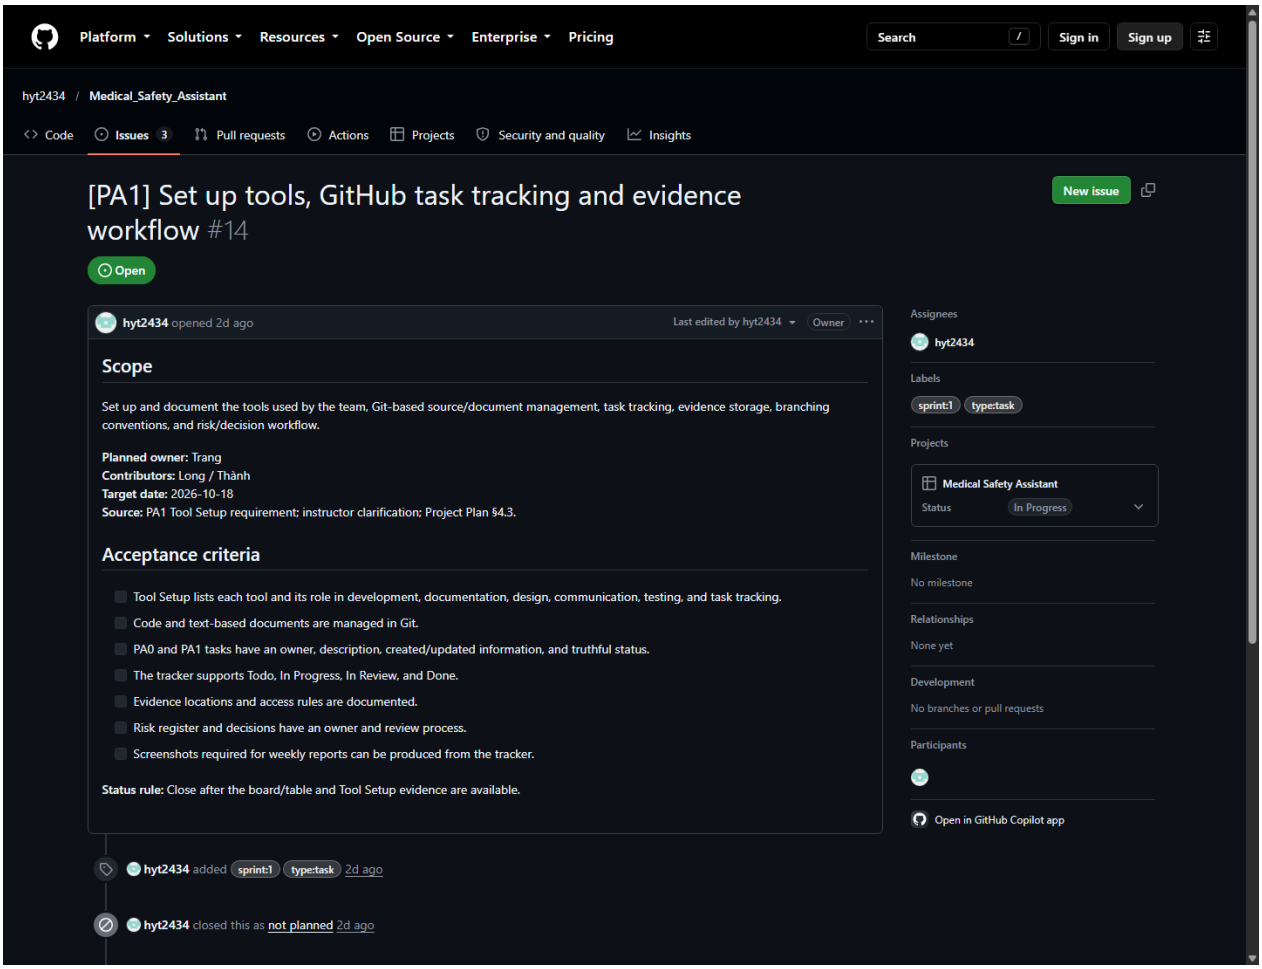


Figure 5: Issue #14: tool setup, task tracking and evidence workflow.
